RESET FORM

HOLLOW METAL FRAME ORDER

Frame specification, anchors, hardware preparation & locations

559 King Forest Court, Burlington, Ontario L7P 5C1
Tel (905) 335-1638 | Fax (905) 335-6822 | Toll Free 1-866-769-3667

Complete one sheet per frame type. Blank fields use the standard listed on page 2. Dimensions accept 84, 83-1/8, 83 1/8, 83.125 or 7'0.

CUSTOMER	CONTACT	PHONE	EMAIL

PROJECT / JOB NAME	P.O. #	QUOTE #	DATE REQUIRED	FRAME MARK / TAG(S)

FRAME

HANDING	QTY	FRAME TAGS
LH		
RH		
LHR		
RHR		
PAIR		
DBL EGRESS		

Handing viewed from the outside (keyed / secure side).

FRAME TYPE	OPENING W	OPENING H	CUSTOM H
Drywall - knocked down (DW)		7/0 (84")	


Opening = frame rebate / nominal door size (e.g. 36 x 84). Pairs: overall rebate width.

WALL THICKNESS	JAMB DEPTH (AUTO)	PROFILE
		Double rabbet - unequal

DOOR THK.	GAUGE	HINGE JAMB	HEADER	STRIKE JAMB
1-3/4"	16 ga	2"	2"	2"

MATERIAL	BOTTOM	FIRE RATING
Galvanneal A40 (standard)	Floor anchors (std)	Non-rated

PROFILE & ANCHORS

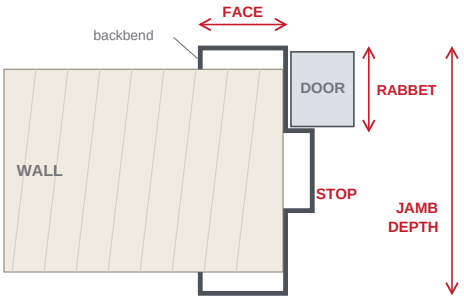

Plan section through jamb, wraparound (typical) - updates with profile.

STOP HEIGHT	DOOR RABBET
5/8"	

OPP. RABBET	BACKBEND
	1/2"

KERF
No kerf (standard)

Door rabbet = door thickness + 3/16".

WALL CONSTRUCTION
Steel stud & drywall

JAMB ANCHORS
None

ANCHORS PER JAMB	BASE ANCHOR
Standard	Floor anchor (std)

MORTAR GUARDS	GROUT FILL
Standard	By others

TRANSOM / SIDELITE / MULLION (IF APPLICABLE)

TRANSOM	TRANSOM H	SIDELITE	SIDELITE W	OVERALL W x H (AUTO)
None		None		

MULLION	MULLION FACE	GLAZING STOPS	GLASS
None		Removable - secure side in	By others

SIDELITE BOTTOM RAIL (BASE)	SIDELITE MID RAIL	MID RAIL CL ABOVE FLOOR
2"	None	

Mid rail CL measured from finished floor.

ELECTRIFIED PREPS

- ☐ Electric hinge / EPT
- ☐ Electric strike box
- ☐ Door position switch (head)
- ☐ Junction box (head)
- ☐ Card reader box (jamb)
- ☐ Mag lock reinf. (head)

EPT AT HINGE #	ELECTRIFIED NOTES

ANCHOR DETAIL

No jamb anchors

HOLLOW METAL FRAME ORDER

Frame specification, anchors, hardware preparation & locations


559 King Forest Court, Burlington, Ontario L7P 5C1
Tel (905) 335-1638 | Fax (905) 335-6822 | Toll Free 1-866-769-3667

HARDWARE PREPARATION & LOCATIONS

OPENING: Single

HANDING: LH

Viewed from outside, hinge side left.

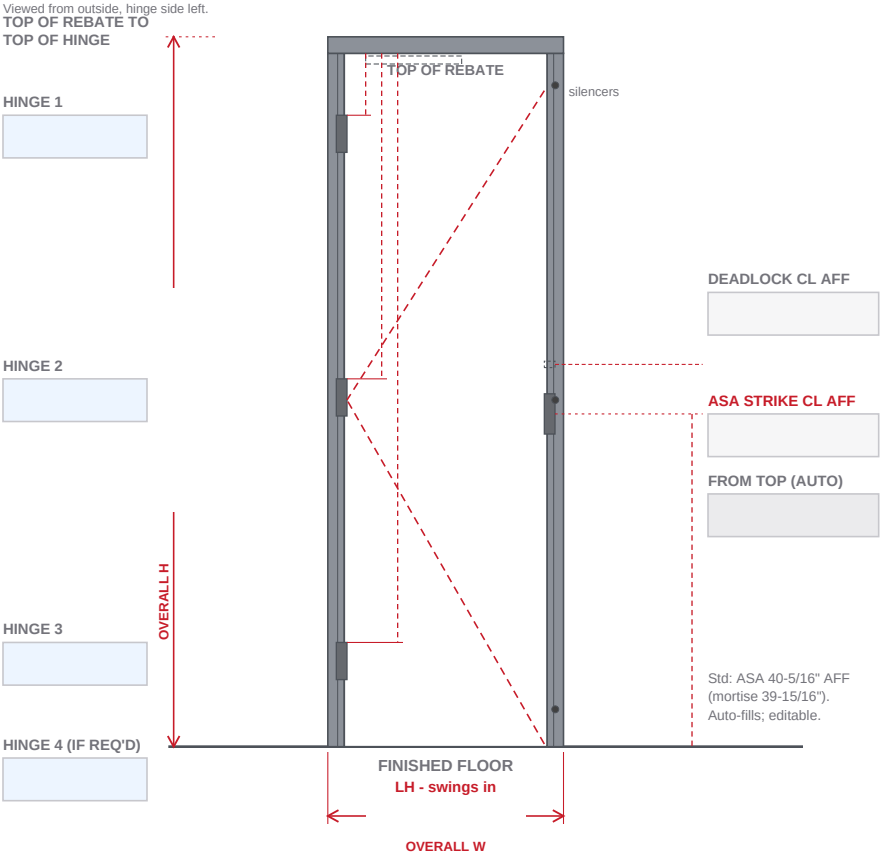

HINGE PREP	SIZE	WEIGHT
Butt hinge - mortised	4-1/2"	Standard

DOOR LOCK TYPE (SETS STRIKE HEIGHT): Cylindrical / rim exit (ASA)

STRIKE PREP: ASA 4-7/8" strike (standard)

HEAD PREP	CLOSER REINF. (HEAD)
None	Standard

SILENCERS	STOP / HOLDER
3 holes (single)	None

GENERAL NOTES / SPECIAL INSTRUCTIONS

STANDARD (UNLESS NOTED)

- Frame: 16 ga galvanneal A40, double rabbet (unequal), 2" faces, 5/8" stop, 1/2" backbend, unfinished; hinge jamb with 10 ga hinge reinforcement.
- Jamb depth = wall thickness + 1" (field verify). Door rabbet = door thickness + 3/16".
- Hinges: 4-1/2" standard weight, 3 to 7'6" opening height, 4 to 10'0". First hinge 7-1/2" from top of rebate to top of hinge; bottom hinge 12-5/8" above finished floor to top of hinge; intermediate equally spaced. (3-1/2": 8" / 12-1/8" 4": 7-3/4" / 12-3/8" 5": 7-1/4" / 12-7/8")
- Strike: ASA 4-7/8" with mortar box, CL 40-5/16" AFF (mortise 39-15/16"); 3 silencer holes on strike jamb (2 in head for pairs).
- Anchors: 3 per jamb up to 7'6", 4 per jamb over 7'6" (masonry wire anchors 6 / 8 per frame); floor anchors standard.
- Fire-rated frames: label, anchors and hardware preps must suit the listing.

APPROVAL

APPROVED BY (PRINT)	SIGNATURE	DATE	ALLDOOR ORDER # (OFFICE)

Please email the completed form to your Alldoor representative. Frames are made to order - please check all sizes before signing.
